

# CompTIA

## Exam Questions PK0-005

CompTIA Project+ Certification Exam



**NEW QUESTION 1**

DRAG DROP -

During a gate review meeting, the deliverable was rejected by the customer.

Review the dashboard.

Part 1: Drag and drop each task, placing them in the correct order based on the project change control process.

Part 2: Select the proper document(s) to be updated.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

 Dashboard

Drag and Drop

Perform a demonstration.

Define new requirements and record changes.

Update and test the deliverable.

Consult the RACI matrix.

Assess the schedule, risk, and cost.

Obtain a sign off.

Make an announcement on the company portal.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

 Dashboard

Question Options

Select the appropriate document(s) to update.

☐

 Risk register

☐

 Schedule

☐

 Statement of work

☐

 Organizational chart

☐

 Change log

☐

 Issues log

☐

 WBS dictionary

- A. Mastered
- B. Not Mastered

**Answer:** A

**Explanation:**

Part 1

Part 2

Change Control Process

1

Define new requirements and record changes.

2

Assess the schedule, risk, and cost.

3

Update and test the deliverable.

4

Perform a demonstration.

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

Dashboard

Drag and Drop

Perform a demonstration.

Define new requirements and record changes.

Update and test the deliverable.

Consult the RACI matrix.

Assess the schedule, risk, and cost.

Obtain a sign off.

Make an announcement on the company portal.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

☒ Statement of work

7

☒ Schedule

8

☒ Change log

Question Options

Select the appropriate document(s) to update.

☐ Risk register

☐ Schedule

☐ Statement of work

☐ Organizational chart

☐ Change log

☐ Issues log

☐ WBS dictionary

### NEW QUESTION 2

During a quality analysis review, the causes of several issues have been highlighted. Which of the following should the project manager use to identify the MOST important causes?

- A. Ishikawa diagram
- B. Scatter diagram
- C. Pareto chart
- D. Decision tree

**Answer: C**

### NEW QUESTION 3

As part of the planning phase, a PM has defined tasks, durations, resources, and costs. Which of the following is the NEXT step in the process?

- A. Update the work breakdown structure.
- B. Review the backlog.
- C. Seek baseline approval.
- D. Establish the resource pool.

**Answer: C**

### NEW QUESTION 4

By developing a project schedule, a PM has already validated the constraints, outlined the duration of the tasks and the phases, and confirmed the proper sequence and flow of the project. Which of the following activities still needs to be performed to complete the schedule?

- A. Allocate resources.
- B. Determine the project budget.
- C. Develop a communication plan.
- D. Establish baselines.

**Answer: D**

### NEW QUESTION 5

During a staff meeting, a project manager voices a concern about the client billing rate for a particular engineer. Which of the following documents would the project manager need in order to find this information?

- A. SLA

- B. TOR
- C. SOW
- D. NDA

**Answer:** AB

#### NEW QUESTION 6

During the stabilization phase for recently deployed software, an end user reports a bug that is compromising data integrity. Which of the following tools will the project manager MOST likely use?

- A. Issue log
- B. Defect log
- C. Change log
- D. Task board

**Answer:** B

#### NEW QUESTION 7

A project manager has been very diligent in maintaining the version control for the documentation of requirements. Which of the following tools is the project manager using?

- A. Multiauthoring software
- B. Word processor
- C. Real-time polling
- D. Conferencing platforms

**Answer:** A

#### NEW QUESTION 8


Due to budgetary and time constraints, a PM scheduled a meeting with all stakeholders during the planning phase to review the requirements and come to an agreement on the minimum viable product that would be acceptable. Which of the following would be used to document this input?

- A. Project change management plan
- B. Project management plan Most Voted
- C. Project transition plan
- D. Project communication plan

**Answer:** B

#### NEW QUESTION 9

A project team was instructed to refurbish old desktops. The following provides the details of the issues observed:

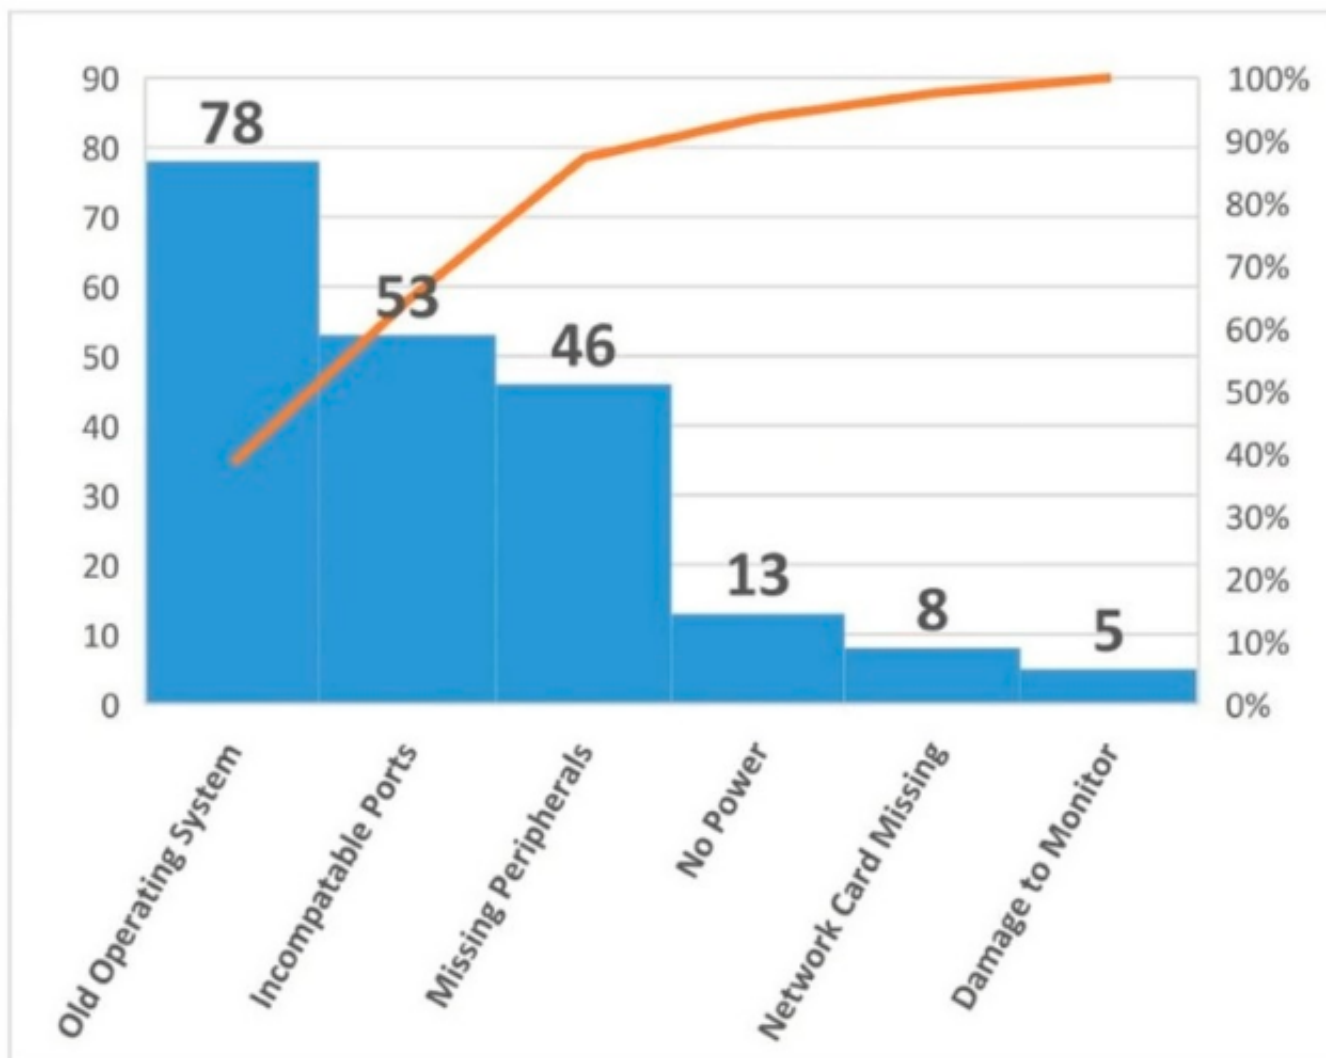

- A. Replace missing peripherals because this process can be easy and less costly.
- B. An old operating system issue has the most amount of occurrences.
- C. Damage to the monitor has the highest percentage.
- D. Address each issue as discovered to avoid rework.

**Answer:** A

**NEW QUESTION 10**

A project manager was not part of a contract negotiation. The project manager is concerned that stakeholders will expect the project to achieve deliverables requested in the RFP. Which of the following documents should the project manager produce FIRST to start communication about the boundaries of the project?

- A. Milestone chart
- B. Work breakdown structure
- C. Project charter
- D. Detailed scope statement

**Answer:** C

**NEW QUESTION 10**

In a functional organization, a project has been completed successfully. Which of the following actions would the project manager MOST likely perform?

- A. Assemble a new project with existing resources.
- B. Obtain the final report from release management.
- C. Notify the functional manager that resources are released.
- D. Allocate resources in a different project.

**Answer:** B

**NEW QUESTION 15**

A third party needs to perform a short-term task for which the duration cannot be accurately estimated and the cost cannot be calculated in advance. Which of the following should the project manager put in place before work begins?

- A. Time and materials contract
- B. Master service agreement
- C. Fixed-price contract
- D. Statement of work
- E. Cost-plus agreement

**Answer:** A

**NEW QUESTION 16**

A company that is implementing an updated version of its main product hired a new project manager to lead the project. Prior to the start of the project, the sponsor asked the project manager to prepare a report on the defects found in the previous project to avoid a decrease in production. The report shows that the two main defects are related to cosmetic and physical damage to the product. Which of the following charts would BEST prioritize which defects to address?

- A. Pareto
- B. Run
- C. Control
- D. Histogram

**Answer:** A

**NEW QUESTION 21**

Which of the following is a quality assurance tool?

- A. Defining project goals
- B. Identifying the root cause analysis
- C. Assessing employee efficiency
- D. Assessing skill gaps

**Answer:** D

**NEW QUESTION 22**

A project manager sent equipment to a global project team for testing purposes. Only 70% of the project team received the equipment for testing. Which of the following considerations is impacting the rest of the team?

- A. Quality assurance
- B. Organizational branding restrictions
- C. State privacy acts
- D. Country legal regulations

**Answer:** D

**NEW QUESTION 27**

A project manager has been assigned to a new project. During the planning phase, the project manager needs to get an understanding of the purpose of the project. Which of the following should the project manager do?

- A. Collate the lessons learned.
- B. Perform a gap analysis.
- C. Review existing artifacts.

D. Conduct a retrospective.

**Answer: C**

#### NEW QUESTION 28


Someone claiming to be from a tax agency sent an email to a team member asking for access to the project repository. Which of the following BEST describes this scenario?

- A. Social engineering
- B. Phishing
- C. Spoofing
- D. Hacking

**Answer: B**

#### NEW QUESTION 30

A project team evaluated the performance of a new reporting system and the quantity of queries to be processed during predetermined time stamps.

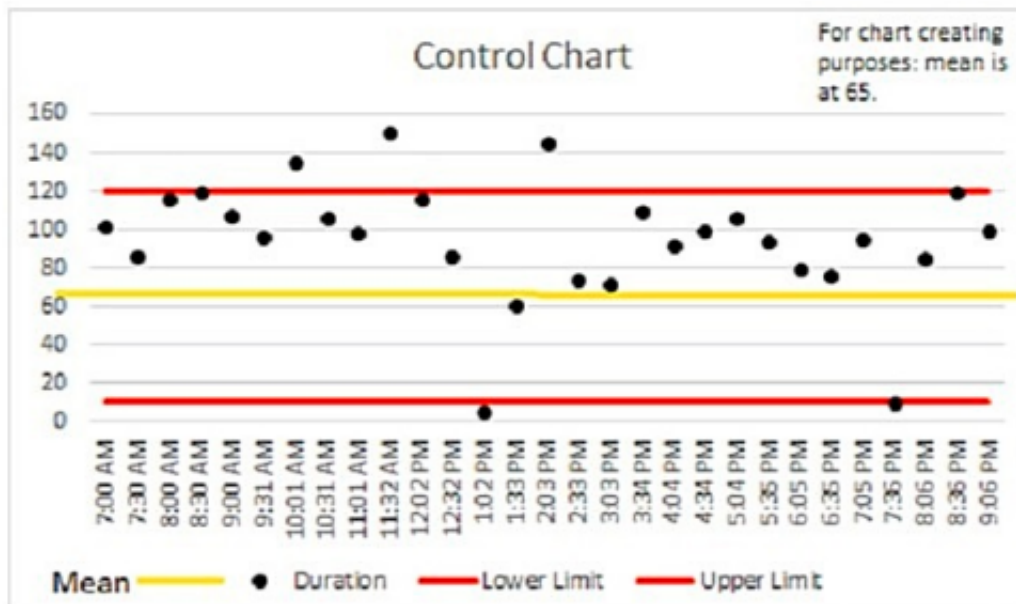

Which of the following is the current status of the process?

- A. Based on the rule of seven, the process is under control.
- B. The amount of data is insufficient to determine if quality is low.
- C. The process is out of control and should be revised.
- D. The goal should be adjusted since most of the data points are close to the lower limit.

**Answer: C**

#### NEW QUESTION 34

An opportunity emerged in the middle of a project life cycle. Which of the following is the BEST action for the project manager to take?

- A. Exploit the risk.
- B. Accept the risk.
- C. Avoid the risk.
- D. Transfer the risk.

**Answer: D**

#### NEW QUESTION 39

A program manager is reviewing the project portfolio and prioritizing each project based on the company's strategic plan. Which of the following should be considered in this evaluation? (Choose two.)

- A. Company vision
- B. Global environment
- C. Brand value
- D. Mission statement
- E. Portfolio budget
- F. Local legislation

**Answer: AB**

#### NEW QUESTION 41

A visual that displays team progress was created for stand-up meetings. Which of the following BEST describes what is being represented on the visual?

- A. Decision board
- B. Whiteboard
- C. Task board
- D. Dashboard

**Answer: D**



#### NEW QUESTION 44

A project manager is assigned to a multinational project with team members from different continents. Which of the following is the MOST important aspect for the project manager to consider?

- A. Resource allocation
- B. Communication security
- C. Technological factors
- D. Cultural differences

**Answer: D**

#### NEW QUESTION 49

Which of the following describes three-tier architecture?

- A. Conceptual, design, and implementation stages
- B. Presentation, application, and data processing
- C. Network, software, and security
- D. Development, testing, and production environment

**Answer: B**

#### NEW QUESTION 50


After determining the appropriate maintenance window, which of the following should occur NEXT in the operational infrastructure change process?

- A. Implement the change.
- B. Approve the test plan.
- C. Notify customers.
- D. Develop a rollback plan.

**Answer: B**

#### NEW QUESTION 53

A project sponsor asked the PM to provide a summary of the current financial status. The PM uses the following burn up chart for the analysis:

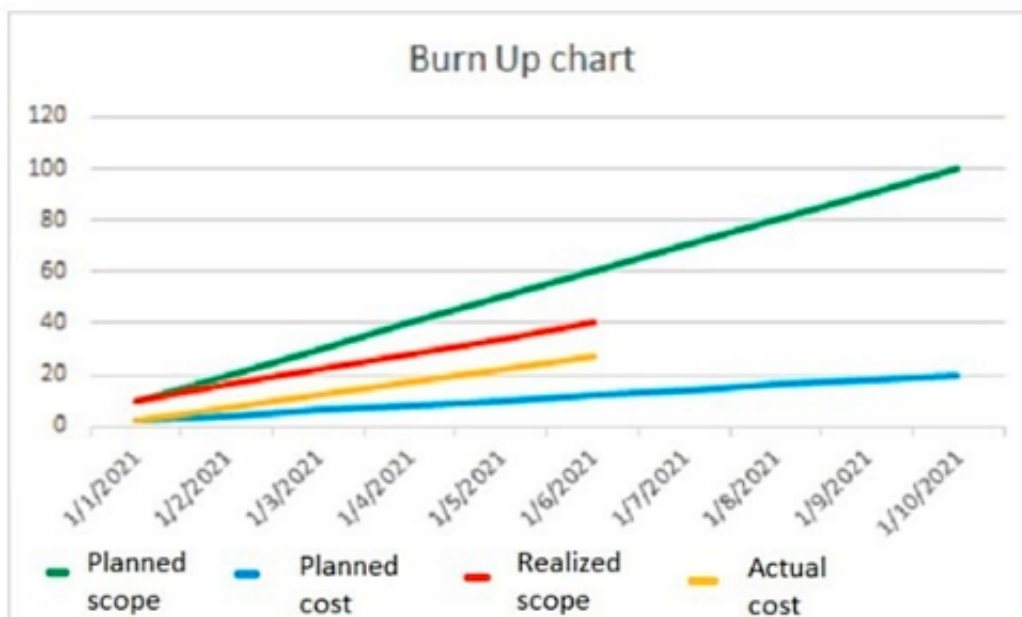

Based on the chart, which of the following is the current status of the project?

- A. Behind schedule and over budget
- B. Behind schedule and under budget
- C. Ahead of schedule and over budget
- D. Ahead of schedule and under budget

**Answer: B**

#### NEW QUESTION 55

.....

## Thank You for Trying Our Product

### We offer two products:

1st - We have Practice Tests Software with Actual Exam Questions

2nd - Questions and Answers in PDF Format

### PK0-005 Practice Exam Features:

- \* PK0-005 Questions and Answers Updated Frequently
- \* PK0-005 Practice Questions Verified by Expert Senior Certified Staff
- \* PK0-005 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- \* PK0-005 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year

**100% Actual & Verified — Instant Download, Please Click**  
**[Order The PK0-005 Practice Test Here](#)**
