

PK0-005 Dumps

CompTIA Project+ Certification Exam

<https://www.certleader.com/PK0-005-dumps.html>



NEW QUESTION 1

By developing a project schedule, a PM has already validated the constraints, outlined the duration of the tasks and the phases, and confirmed the proper sequence and flow of the project. Which of the following activities still needs to be performed to complete the schedule?

- A. Allocate resources.
- B. Determine the project budget.
- C. Develop a communication plan.
- D. Establish baselines.

Answer: D

NEW QUESTION 2

A project manager is in the closing phase of an IT asset refresh project that involves the disposal of several computers. The project sponsor notified the project manager that the company recently received a penalty as a result of disposing of some computers improperly. Which of the following should have been considered during initial planning to prevent this situation?

- A. ESG
- B. PHI
- C. PII
- D. ROIL

Answer: A

NEW QUESTION 3

The project team determines that software installation can only begin after the desktops have been installed and can be powered on. Which of the following dependencies does this represent?

- A. External
- B. Internal
- C. Mandatory
- D. Discretionary

Answer: B

NEW QUESTION 4

Due to budgetary and time constraints, a PM scheduled a meeting with all stakeholders during the planning phase to review the requirements and come to an agreement on the minimum viable product that would be acceptable. Which of the following would be used to document this input?

- A. Project change management plan
- B. Project management plan Most Voted
- C. Project transition plan
- D. Project communication plan

Answer: B

NEW QUESTION 5

A project manager was not part of a contract negotiation. The project manager is concerned that stakeholders will expect the project to achieve deliverables requested in the RFP. Which of the following documents should the project manager produce FIRST to start communication about the boundaries of the project?

- A. Milestone chart
- B. Work breakdown structure
- C. Project charter
- D. Detailed scope statement

Answer: C

NEW QUESTION 6

In a functional organization, a project has been completed successfully. Which of the following actions would the project manager MOST likely perform?

- A. Assemble a new project with existing resources.
- B. Obtain the final report from release management.
- C. Notify the functional manager that resources are released.
- D. Allocate resources in a different project.

Answer: B

NEW QUESTION 7

Which of the following would be MOST beneficial to do before a call to ensure all meeting items are addressed and the correct participants attend?

- A. Assign action items to attendees.
- B. Distribute an agenda
- C. Most Voted
- D. Email the minutes from the previous meeting.
- E. Schedule a convenient time.

Answer: B

NEW QUESTION 8

Which of the following activities would a project manager perform during the closing phase? (Choose three.)

- A. Lessons learned
- B. Risk analysis
- C. Removing resources
- D. Acquiring resources
- E. Statement of work sign-off
- F. Stakeholder analysis
- G. Removing access

Answer: AEF


NEW QUESTION 9


As a result of an approved change, the project manager updates the project plan with the newest project end date. Which of the following change control processes should the project manager complete NEXT?

- A. Document the request in the change control log.
- B. Communicate the change deployment.
- C. Conduct an impact assessment.
- D. Implement the change.

Answer: C

Explanation:

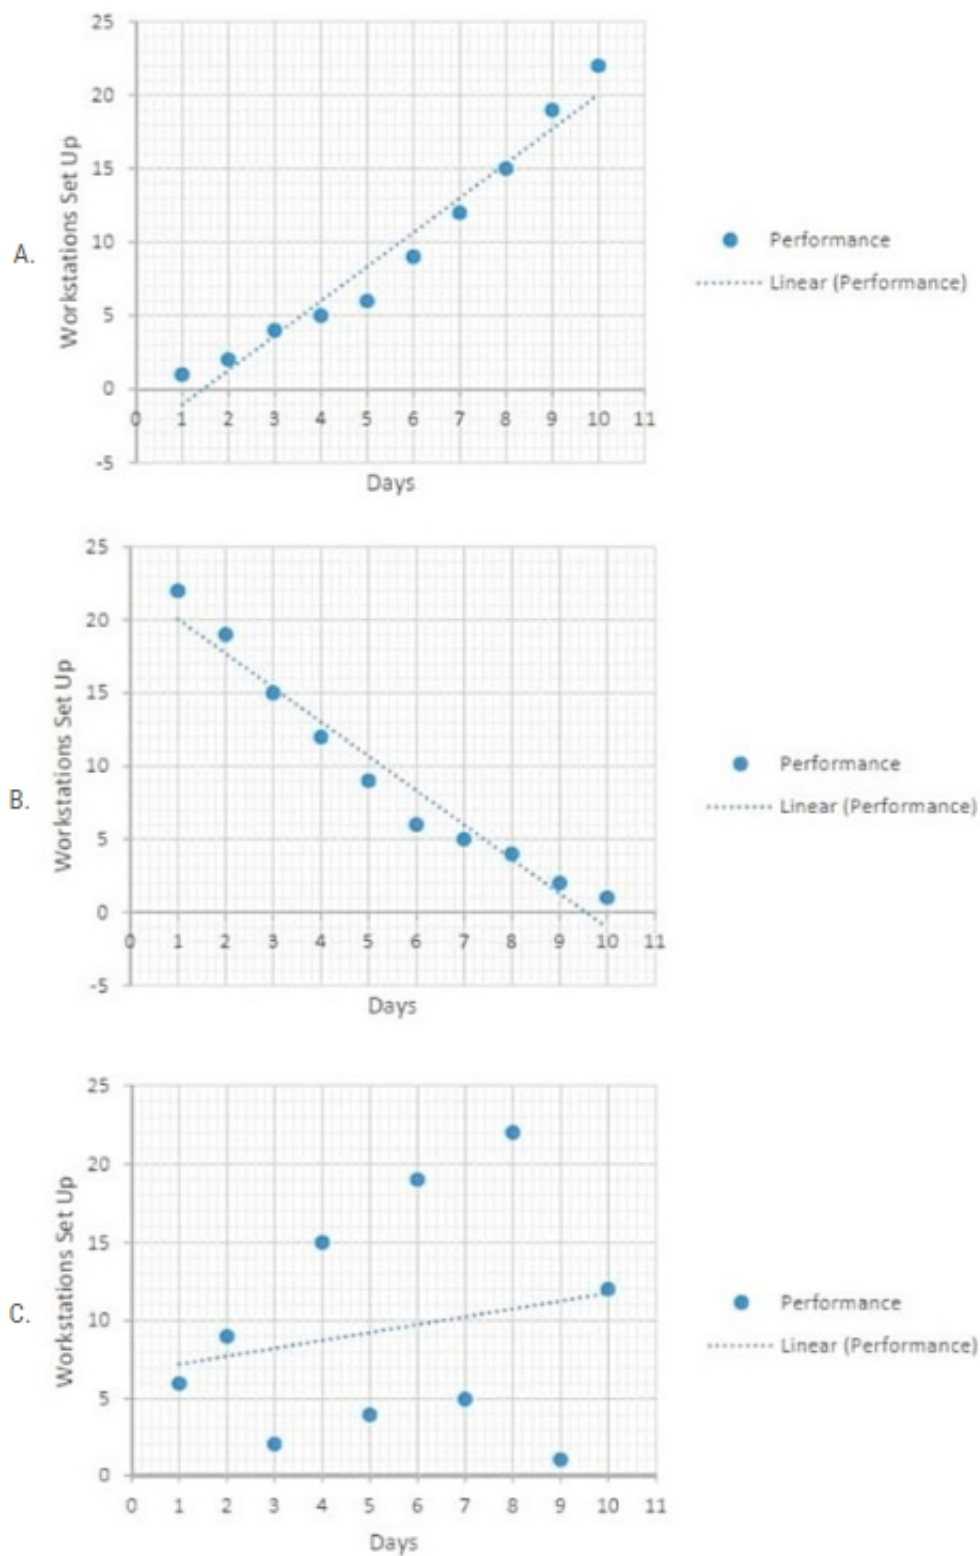

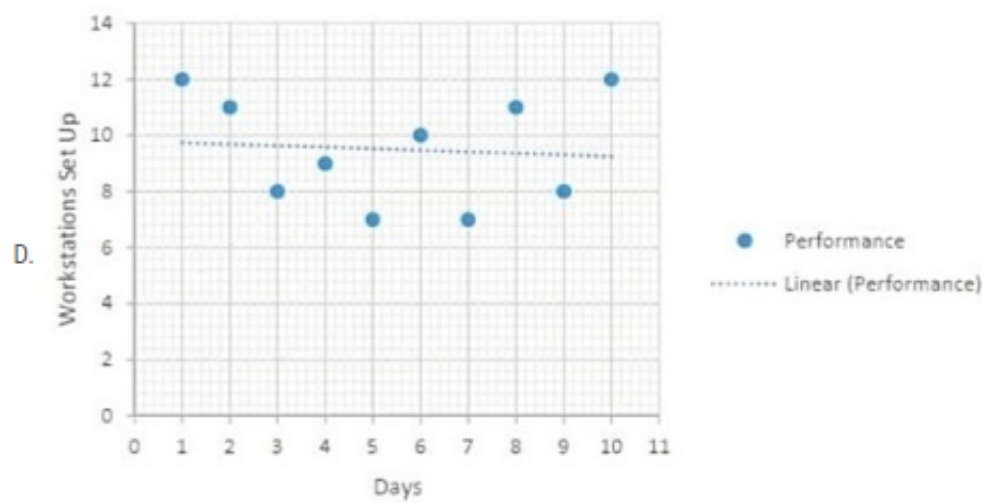

NEW QUESTION 10

A program manager is reviewing the project portfolio and prioritizing each project based on the company's strategic plan. Which of the following should be considered in this evaluation? (Choose two.)

- A. Company vision
- B. Global environment
- C. Brand value
- D. Mission statement
- E. Portfolio budget
- F. Local legislation

Answer: AB

NEW QUESTION 10


Which of the following describes three-tier architecture?

- A. Conceptual, design, and implementation stages
- B. Presentation, application, and data processing
- C. Network, software, and security
- D. Development, testing, and production environment

Answer: B

NEW QUESTION 12

A project sponsor asked the PM to provide a summary of the current financial status. The PM uses the following burn up chart for the analysis:

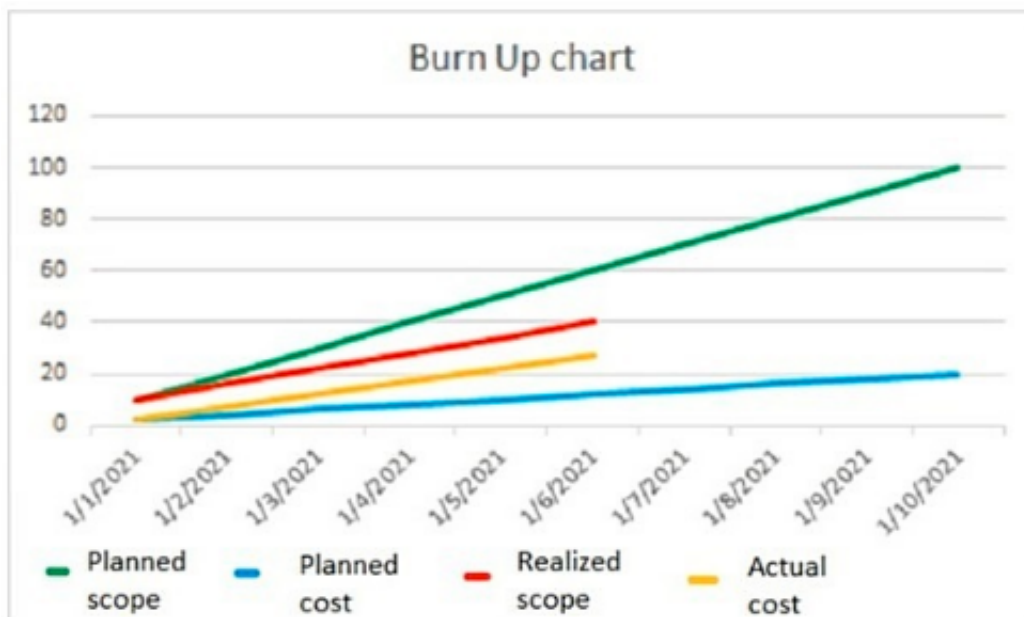

Based on the chart, which of the following is the current status of the project?

- A. Behind schedule and over budget
- B. Behind schedule and under budget
- C. Ahead of schedule and over budget
- D. Ahead of schedule and under budget

Answer: B

NEW QUESTION 17

.....

Thank You for Trying Our Product

* 100% Pass or Money Back

All our products come with a 90-day Money Back Guarantee.

* One year free update

You can enjoy free update one year. 24x7 online support.

* Trusted by Millions

We currently serve more than 30,000,000 customers.

* Shop Securely

All transactions are protected by VeriSign!

100% Pass Your PK0-005 Exam with Our Prep Materials Via below:

<https://www.certleader.com/PK0-005-dumps.html>
